


Designer:	Derek Queno	Designer Tel:	
Town:	Halifax	Digsafe #:	
Date:	12/3/2025	Road Name:	Lucier Road
Project:	202235	Circuit:	56G1
Scale:	1"=150'	Tel Eng:	
Job Title:	202235 Halifax V63 PG.1	Traffic Control:	
		Billing Code:	

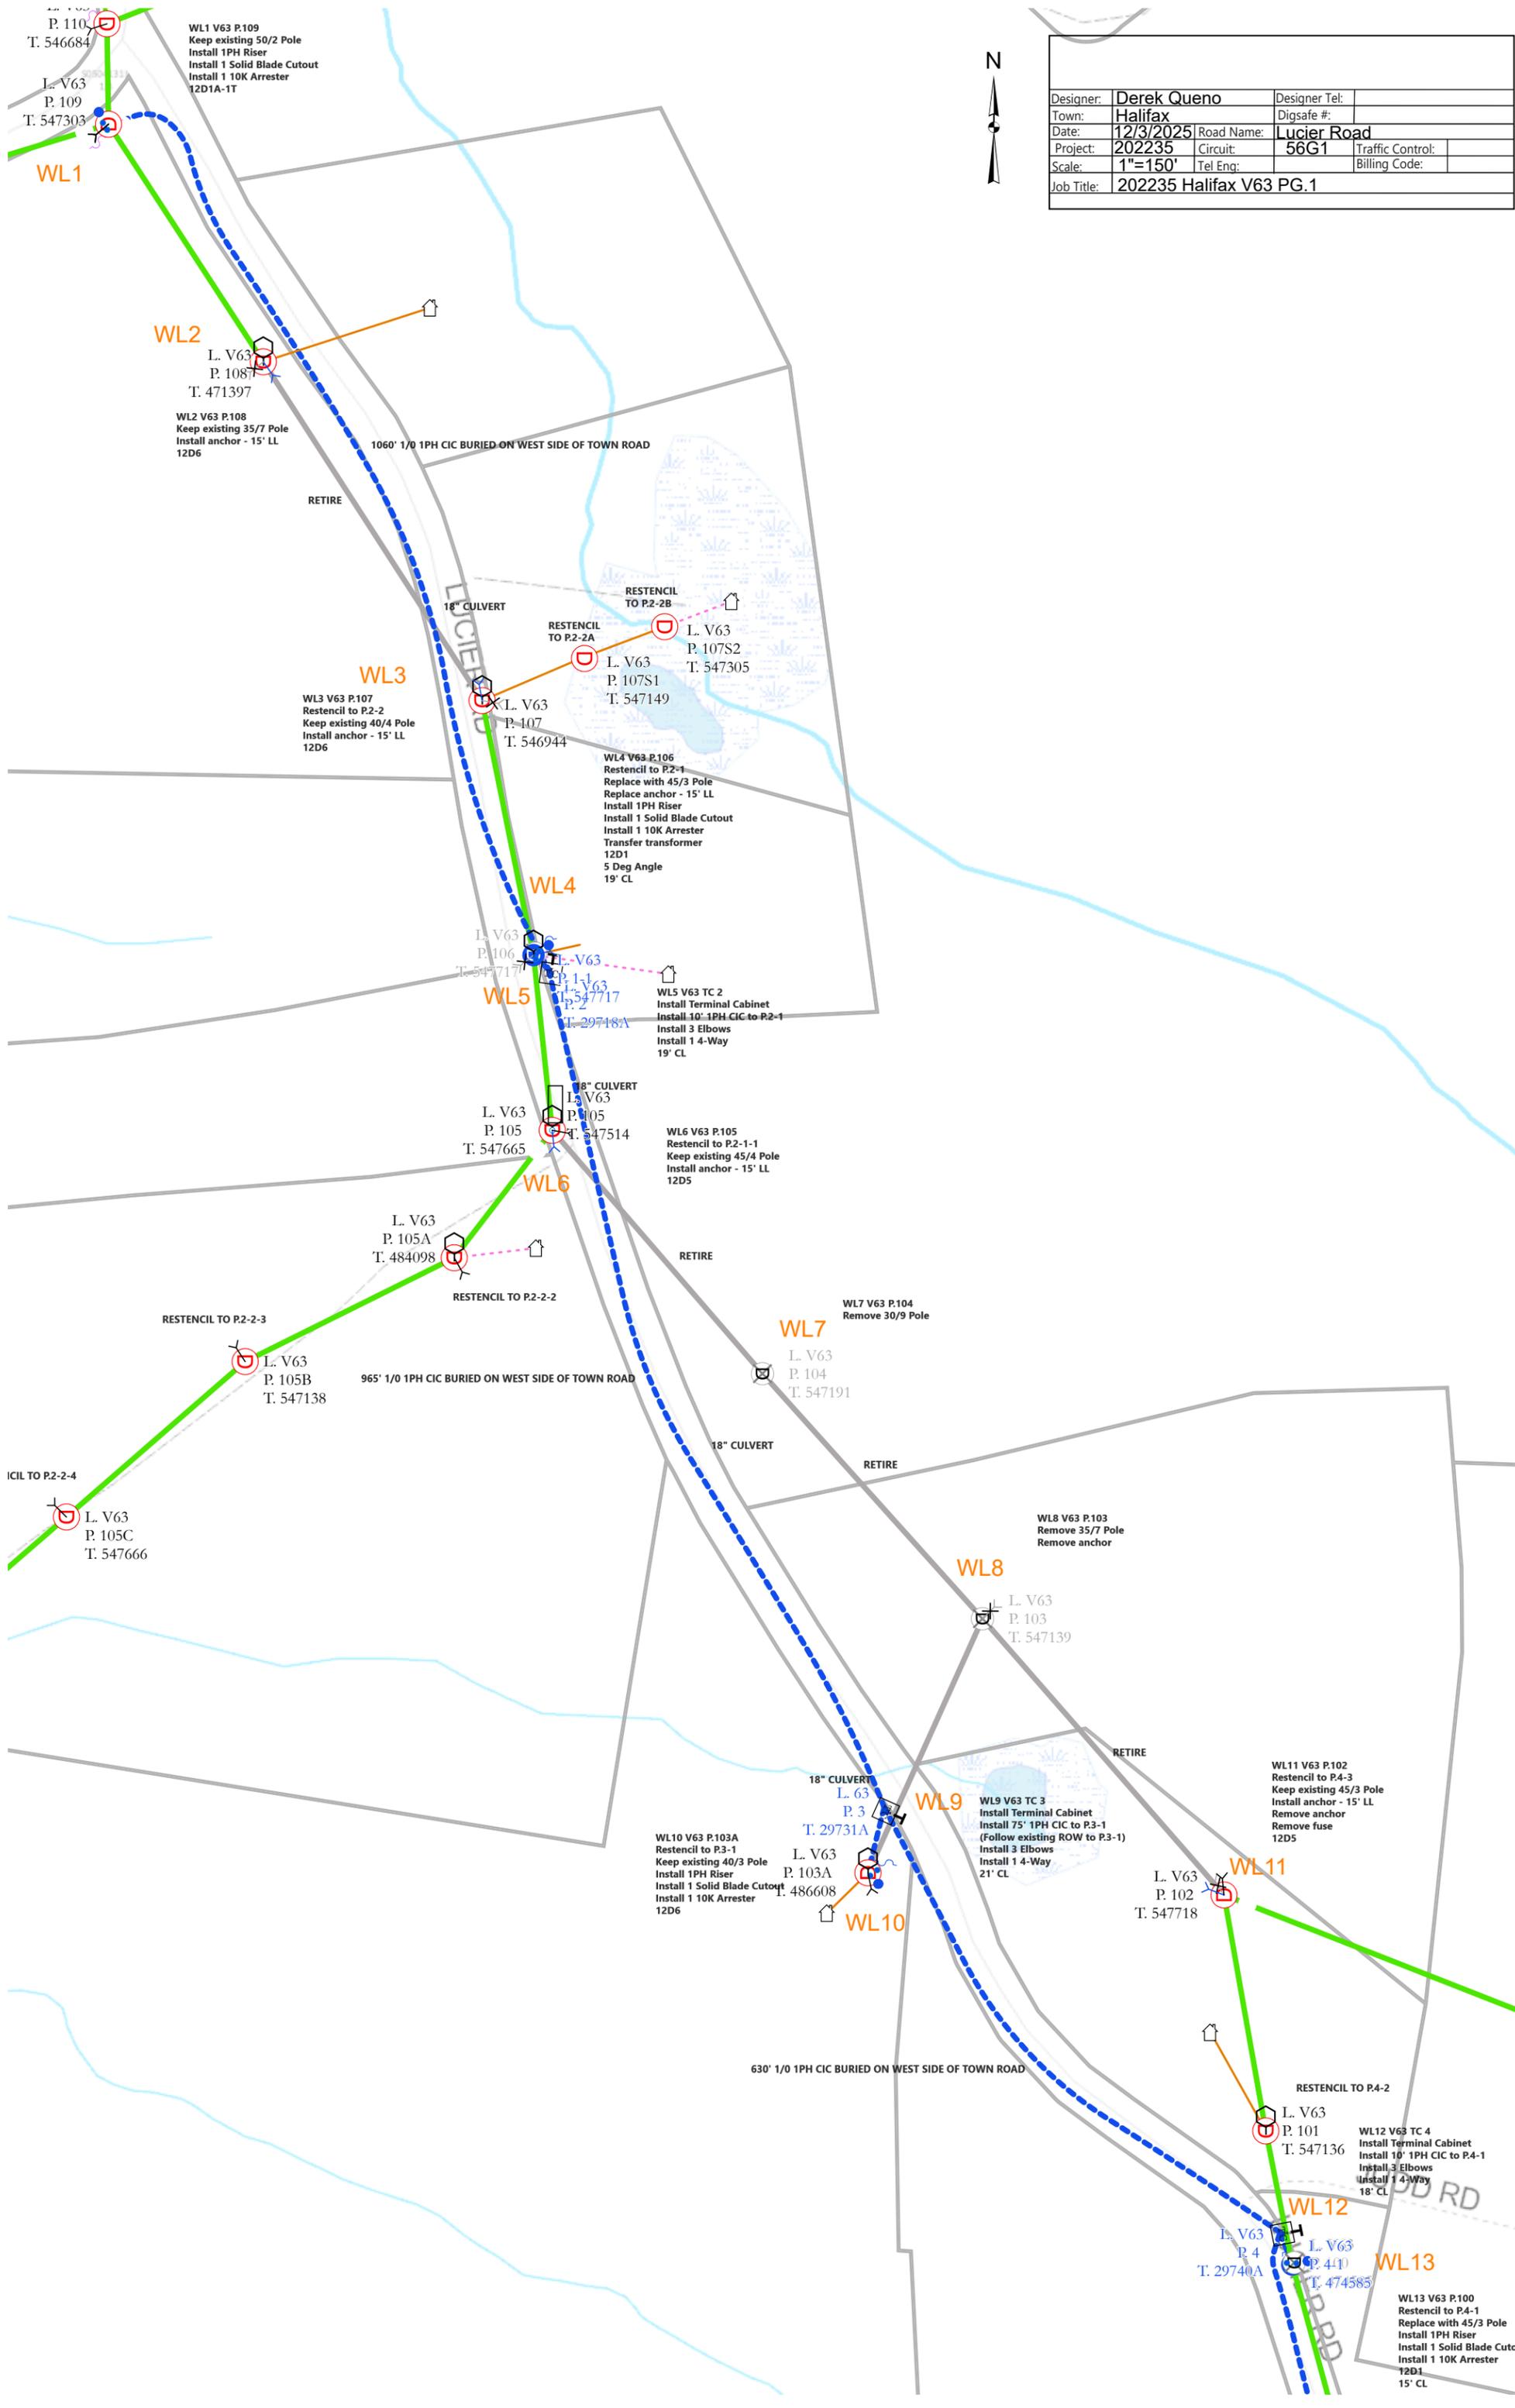

P. 110
T. 546684
L. V63
P. 109
T. 547303

WL1 V63 P.109
Keep existing 50/2 Pole
Install 1PH Riser
Install 1 Solid Blade Cutout
Install 1 10K Arrester
12D1A-1T

WL2
L. V63
P. 1087
T. 471397

WL2 V63 P.108
Keep existing 35/7 Pole
Install anchor - 15' LL
12D6

1060' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

RETIRE

WL3

WL3 V63 P.107
Restencil to P.2-2
Keep existing 40/4 Pole
Install anchor - 15' LL
12D6

18" CULVERT

RESTENCIL TO P.2-2A

RESTENCIL TO P.2-2B

L. V63
P. 107
T. 546944

L. V63
P. 107S1
T. 547149

L. V63
P. 107S2
T. 547305

WL4 V63 P.106
Restencil to P.2-1
Replace with 45/3 Pole
Replace anchor - 15' LL
Install 1PH Riser
Install 1 Solid Blade Cutout
Install 1 10K Arrester
Transfer transformer
12D1
5 Deg Angle
19' CL

WL4

L. V63
P. 106
T. 547171

L. V63
P. 106A
T. 547171

L. V63
P. 106B
T. 297181A

WL5 V63 TC 2
Install Terminal Cabinet
Install 10' 1PH CIC to P.2-1
Install 3 Elbows
Install 1 4-Way
19' CL

WL5

L. V63
P. 105
T. 547514

L. V63
P. 105A
T. 547514

WL6 V63 P.105
Restencil to P.2-1-1
Keep existing 45/4 Pole
Install anchor - 15' LL
12D5

WL6

L. V63
P. 105A
T. 484098

RESTENCIL TO P.2-2-3

L. V63
P. 105B
T. 547138

965' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

18" CULVERT

WL7

L. V63
P. 104
T. 547191

WL7 V63 P.104
Remove 30/9 Pole

ICIL TO P.2-2-4

L. V63
P. 105C
T. 547666

WL8

L. V63
P. 103
T. 547139

WL8 V63 P.103
Remove 35/7 Pole
Remove anchor

18" CULVERT
L. V63
P. 3
T. 29731A

WL9

WL9 V63 TC 3
Install Terminal Cabinet
Install 75' 1PH CIC to P.3-1
(Follow existing ROW to P.3-1)
Install 3 Elbows
Install 1 4-Way
21' CL

WL10 V63 P.103A
Restencil to P.3-1
Keep existing 40/3 Pole
Install 1PH Riser
Install 1 Solid Blade Cutout
Install 1 10K Arrester
12D6

L. V63
P. 103A
T. 486608

WL10

RETIRE

WL11 V63 P.102
Restencil to P.4-3
Keep existing 45/3 Pole
Install anchor - 15' LL
Remove anchor
Remove fuse
12D5

L. V63
P. 102
T. 547718

WL11

630' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

RESTENCIL TO P.4-2

L. V63
P. 101
T. 547136

WL12

WL12 V63 TC 4
Install Terminal Cabinet
Install 10' 1PH CIC to P.4-1
Install 3 Elbows
Install 1 4-Way
18' CL

L. V63
P. 4
T. 29740A


L. V63
P. 410
T. 474585

WL12

WL13

WL13 V63 P.100
Restencil to P.4-1
Replace with 45/3 Pole
Install 1PH Riser
Install 1 Solid Blade Cuto
Install 1 10K Arrester
12D1
15' CL

Designer:	Derek Queno	Designer Tel:	
Town:	Halifax	Digsafe #:	
Date:	12/3/2025	Road Name:	Lucier Road
Project:	202235	Circuit:	56G1
Scale:	1"=150'	Tel Eng:	Blaine@202B
Job Title:	202235 Halifax V63 PG 2	RESTENCIL TO P4-5	T. 547301

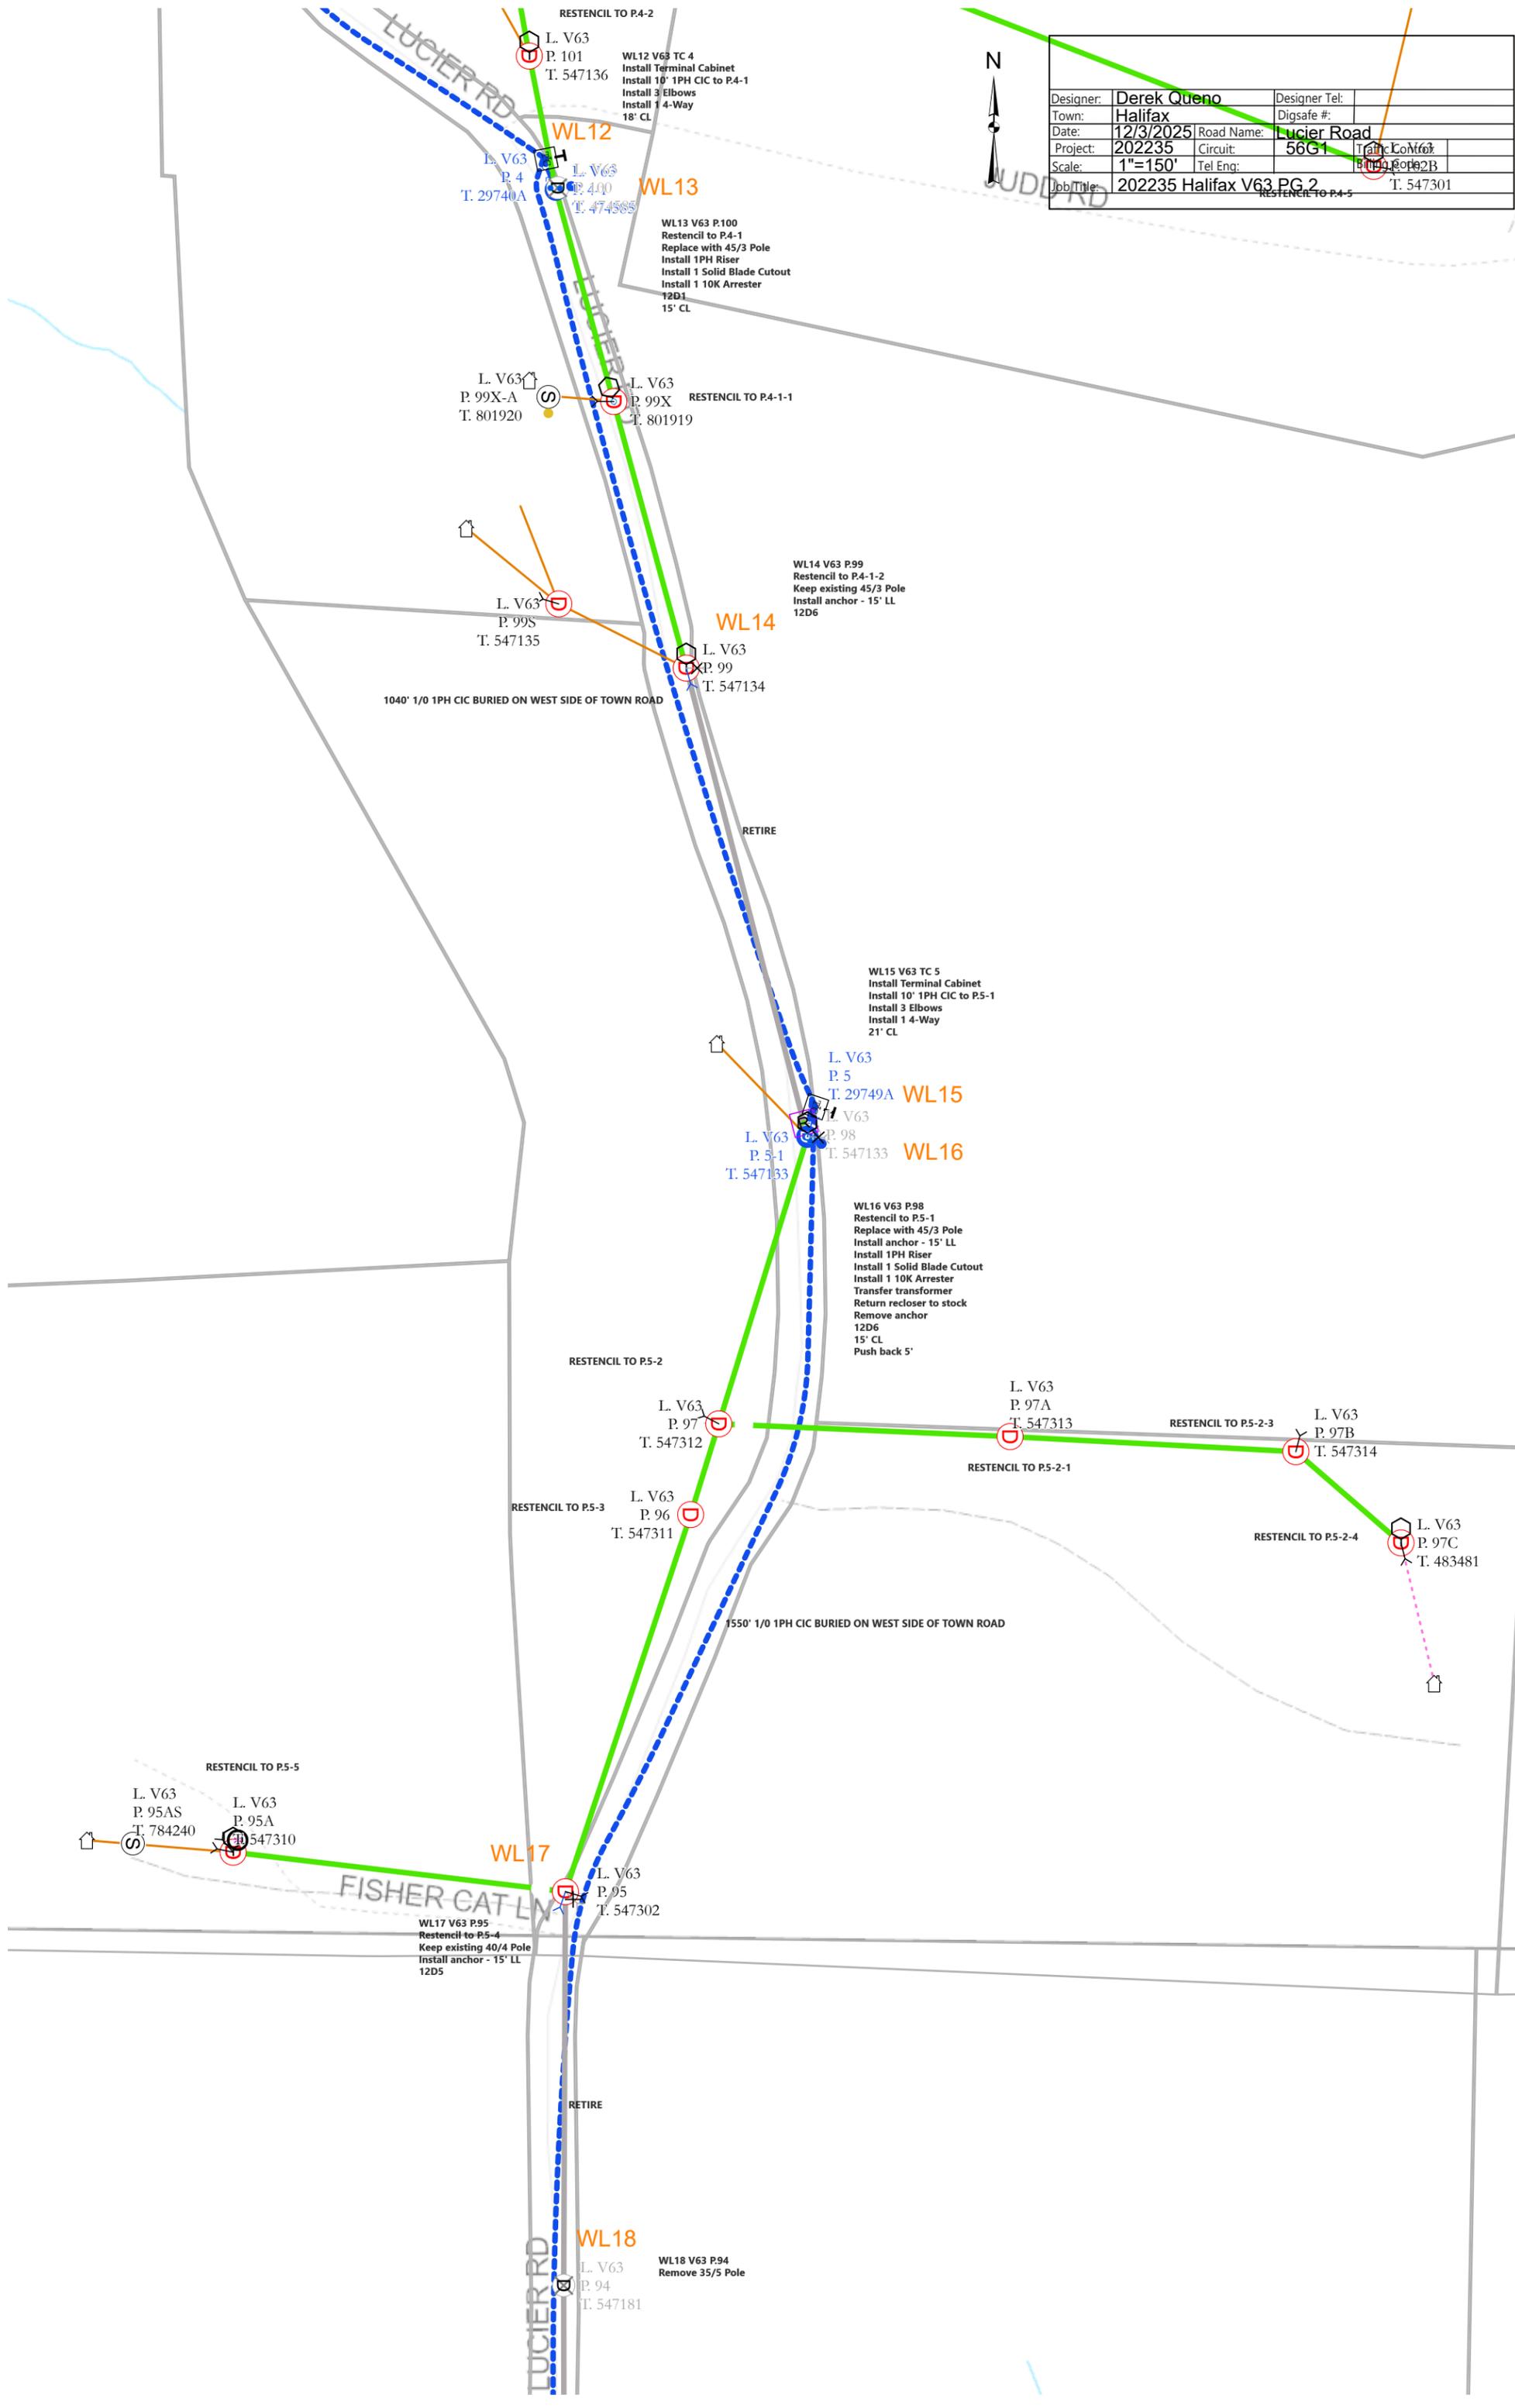

Designer:	Derek Queno	Designer Tel:	
Town:	Halifax	Digsafe #:	
Date:	12/3/2025	Road Name:	Lucier Road
Project:	202235	Circuit:	56G1
Scale:	1"=150'	Tel Eng:	
Job Title:	202235 Halifax V63 PG.3		



WL18
 L. V63
 P. 94
 T. 547181
 WL18 V63 P.94
 Remove 35/5 Pole

RETIRE

WL19
 L. V63
 P. 6
 T. 29757A
 WL19 V63 TC 6
 Install Terminal Cabinet
 Install 2 Elbows
 Install 1 4-Way
 23' CL

WL20 V63 P.93
 Remove 35/4 Pole
 L. V63
 P. 93
 T. 547182

WL20

RETIRE

WL21 V63 P.92
 Remove 35/4 Pole

WL21

L. V63
 P. 92
 T. 547183

15" CULVERT

1510' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

RETIRE

WL22

L. V63
 P. 91
 T. 492240

L. V63
 P. 91
 T. 492205

WL22 V63 P.91
 Remove 40/6 Pole
 Remove 35/5 PB

RETIRE

WL28

L. V63B
 P. 1X
 T. 776909

WL28 V63 P.1X
 Remove 40/3 Pole

RETIRE

WL29 V63 P.2
 Remove 40/4 Pole

WL29

WL30 V63 P.3
 Restencil to F
 Keep existing
 Install anchor
 12D6

WL30

RETIRE

WL23

L. V63
 P. 90X
 T. 492204

WL20 V63 P.90X
 Remove 40/6 Pole
 Remove 35/5 PB

RETIRE

WL27

L. V63B
 P. 1
 T. 547178

WL27 V63 P.1
 Remove 40/3 Pole

RETIRE

WL26

L. V63B
 P. X1
 T. 776908

WL26 V63 P.90
 Remove 35/4 Pole
 Remove anchor

RETIRE

24" CULVERT

WL24

L. V63
 P. 90X
 T. 29761A

WL24 V63 TC 7
 Install Terminal Cabinet
 Install 2 Elbows
 Install 1 4-Way
 24' CL

18" CULVERT

WL25

L. V63
 P. 90
 T. 547285

WL25 V63 P.90
 Remove 35/4 Pole
 Remove anchor

WL31

L. V63
 P. 8
 T. 29765A

WL31 V63 TC 8
 Install Terminal Cabinet
 Install 2 Elbows
 Install 1 4-Way
 24' CL

1220' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD


1220' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

24" CULVERT

CHASE HILL RD

L. V63
 P. 88X
 T. 757588

Designer:	Derek Queno	Designer Tel:	
Town:	Halifax	Digsafe #:	
Date:	12/3/2025	Road Name:	Lucier Road
Project:	202235	Circuit:	56G1
Scale:	1"=150'	Tel Eng:	
Job Title:	202235 Halifax V63 PG.4		

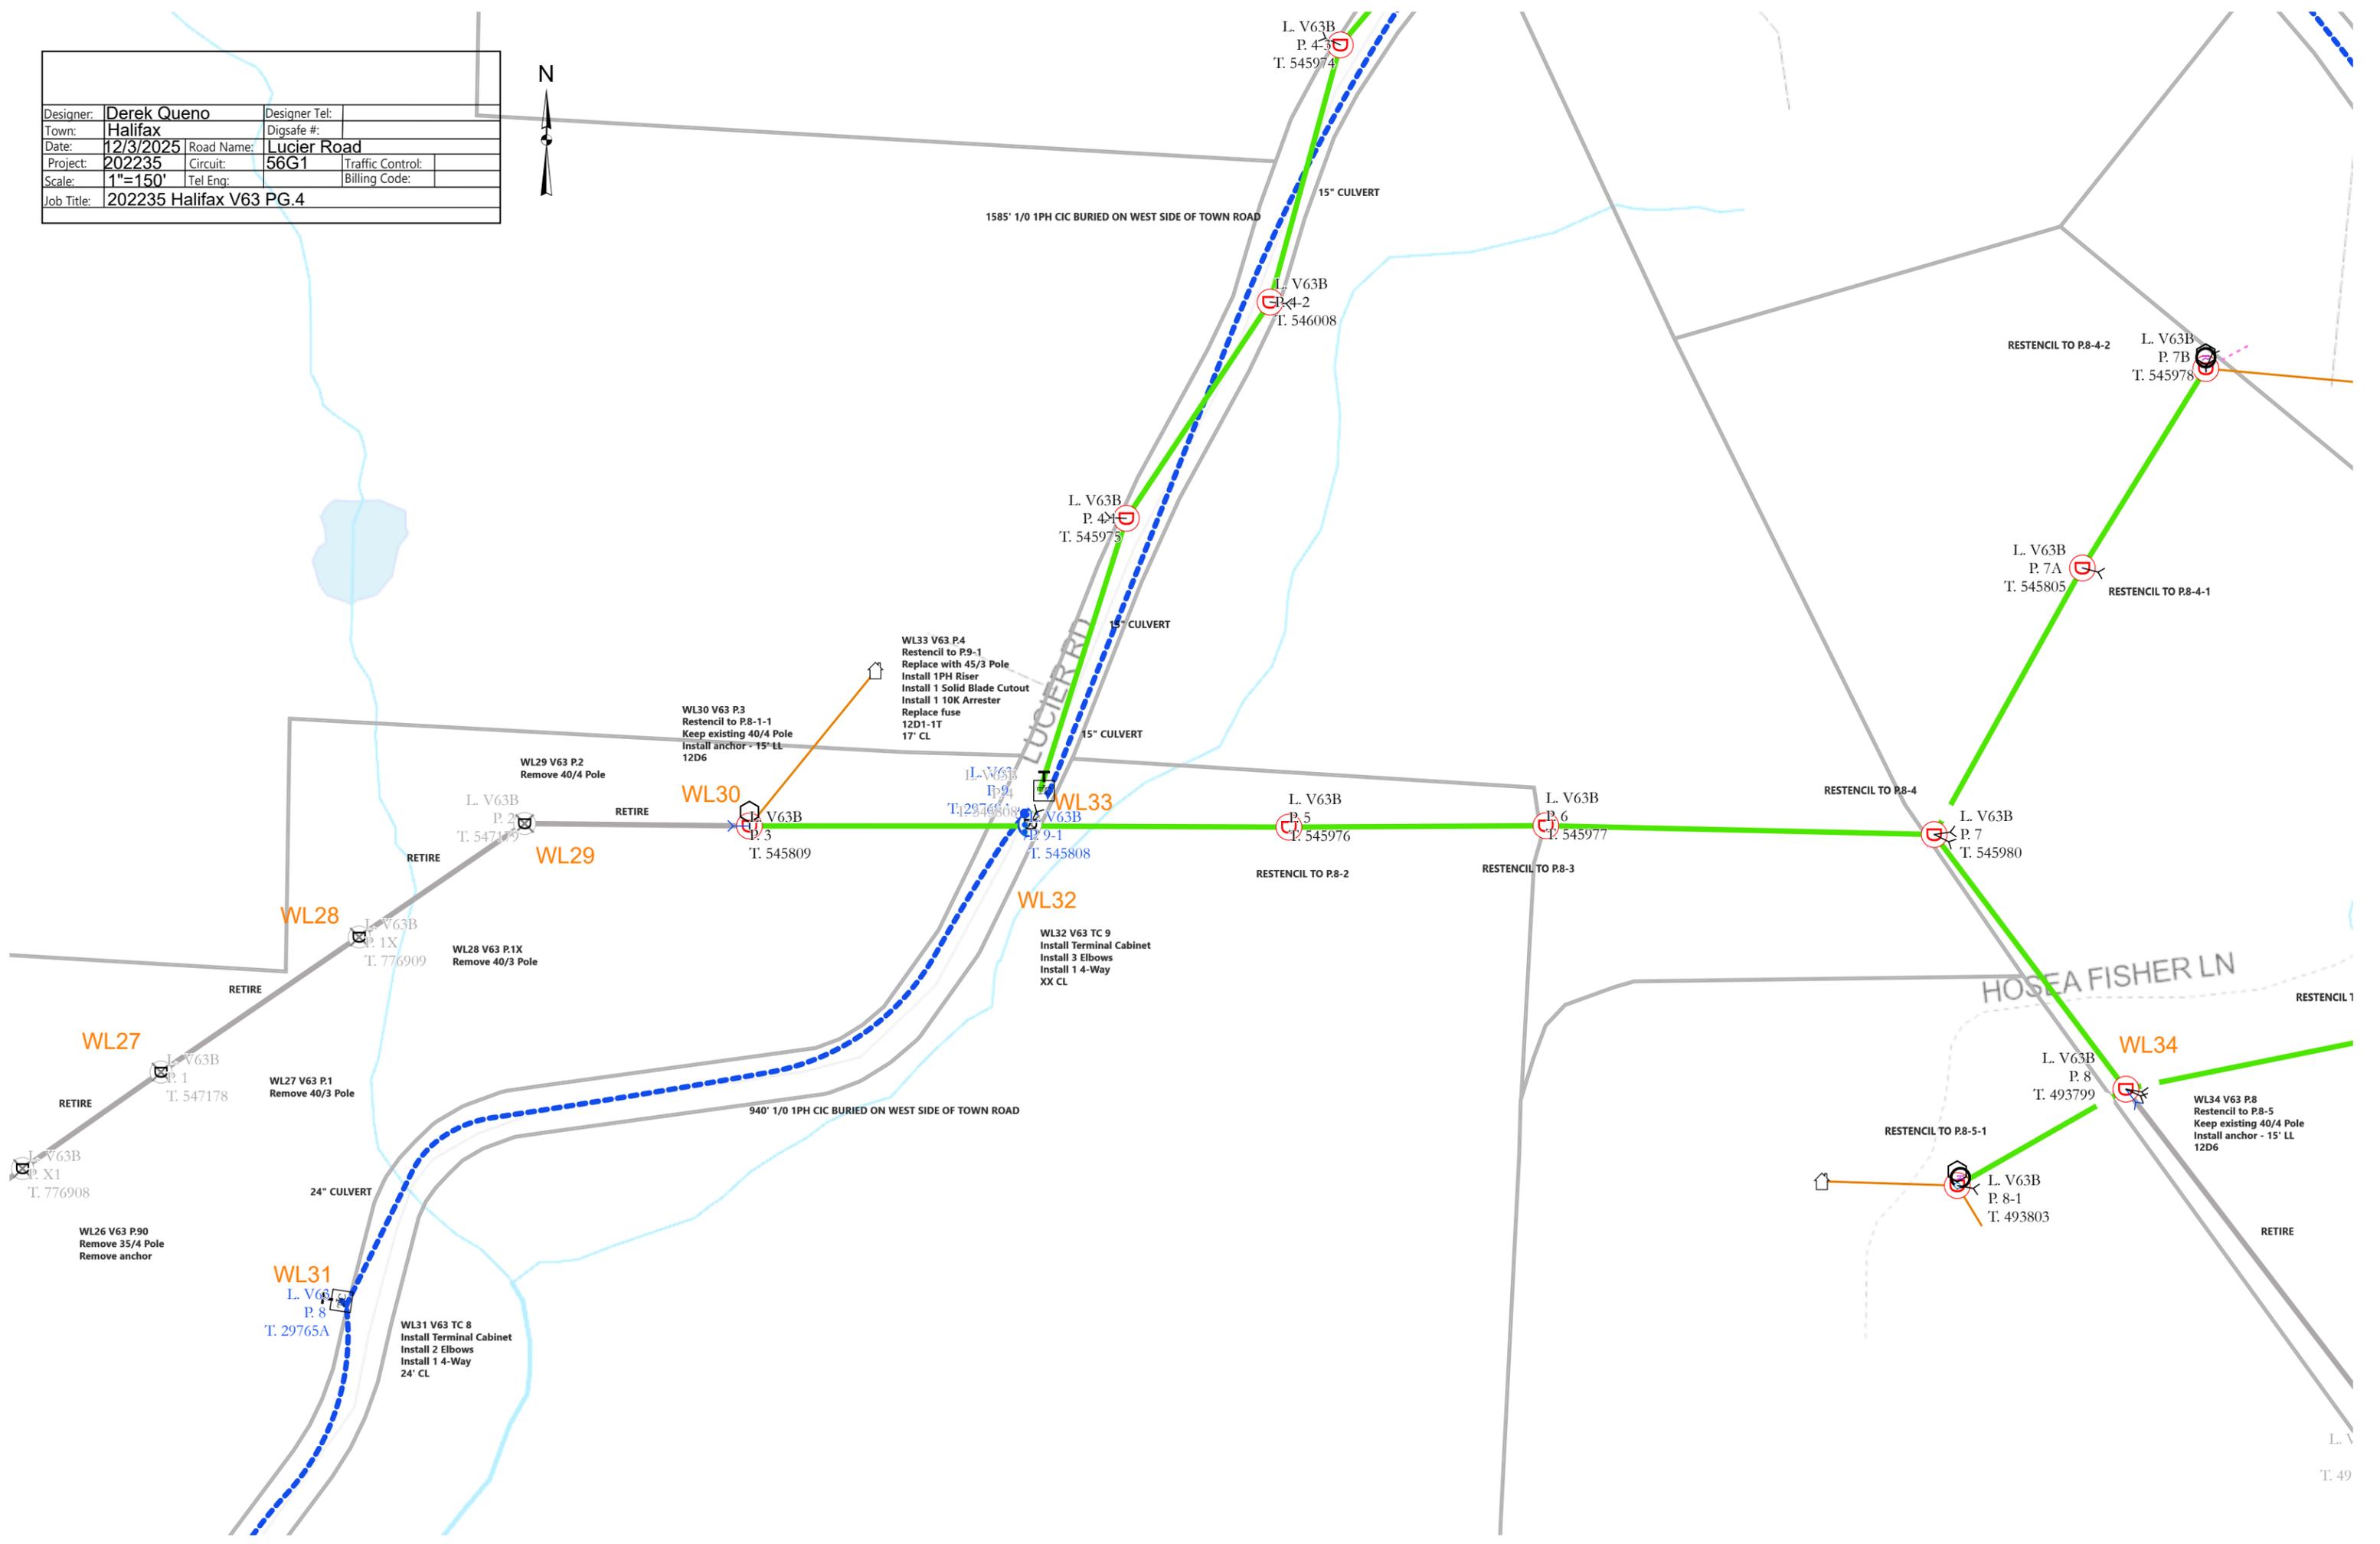

1585' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

15" CULVERT

L. V63B
P. 4-3
T. 545974

L. V63B
P. 4-2
T. 546008

RESTENCIL TO P.8-4-2
L. V63B
P. 7B
T. 545978

L. V63B
P. 7A
T. 545805
RESTENCIL TO P.8-4-1

L. V63B
P. 4-1
T. 545973

WL33 V63 P.4
Restencil to P.9-1
Replace with 45/3 Pole
Install 1PH Riser
Install 1 Solid Blade Cutout
Install 1 10K Arrester
Replace fuse
12D1-1T
17' CL

WL30 V63 P.3
Restencil to P.8-1-1
Keep existing 40/4 Pole
Install anchor - 15' LL
12D6

WL29 V63 P.2
Remove 40/4 Pole

L. V63B
P. 2
T. 547179

WL29

L. V63B
P. 3
T. 545809

WL30

L. V63B
P. 4
T. 545808

L. V63B
P. 9-1
T. 545808

WL32

WL32 V63 TC 9
Install Terminal Cabinet
Install 3 Elbows
Install 1 4-Way
XX CL

L. V63B
P. 5
T. 545976

RESTENCIL TO P.8-2

L. V63B
P. 6
T. 545977

RESTENCIL TO P.8-3

L. V63B
P. 7
T. 545980

RESTENCIL TO P.8-4

WL28

L. V63B
P. 1X
T. 776909

WL28 V63 P.1X
Remove 40/3 Pole

RETIRE

WL27

L. V63B
P. 1
T. 547178

WL27 V63 P.1
Remove 40/3 Pole

RETIRE

L. V63B
P. X1
T. 776908

WL26 V63 P.90
Remove 35/4 Pole
Remove anchor

24" CULVERT

WL31

L. V63B
P. 8
T. 29765A

WL31 V63 TC 8
Install Terminal Cabinet
Install 2 Elbows
Install 1 4-Way
24' CL

940' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

HOSEA FISHER LN

WL34

L. V63B
P. 8
T. 493799

WL34 V63 P.8
Restencil to P.8-5
Keep existing 40/4 Pole
Install anchor - 15' LL
12D6


RESTENCIL TO P.8-5-1

L. V63B
P. 8-1
T. 493803

RETIRE

L. V
T. 49

Designer:	Derek Queno	Designer Tel:	
Town:	Halifax	Digsafe #:	
Date:	12/3/2025	Road Name:	Lucier Road
Project:	202235	Circuit:	56G1
Scale:	1"=150'	Tel Eng:	
Job Title:	202235 Halifax V63 PG.6	Billing Code:	

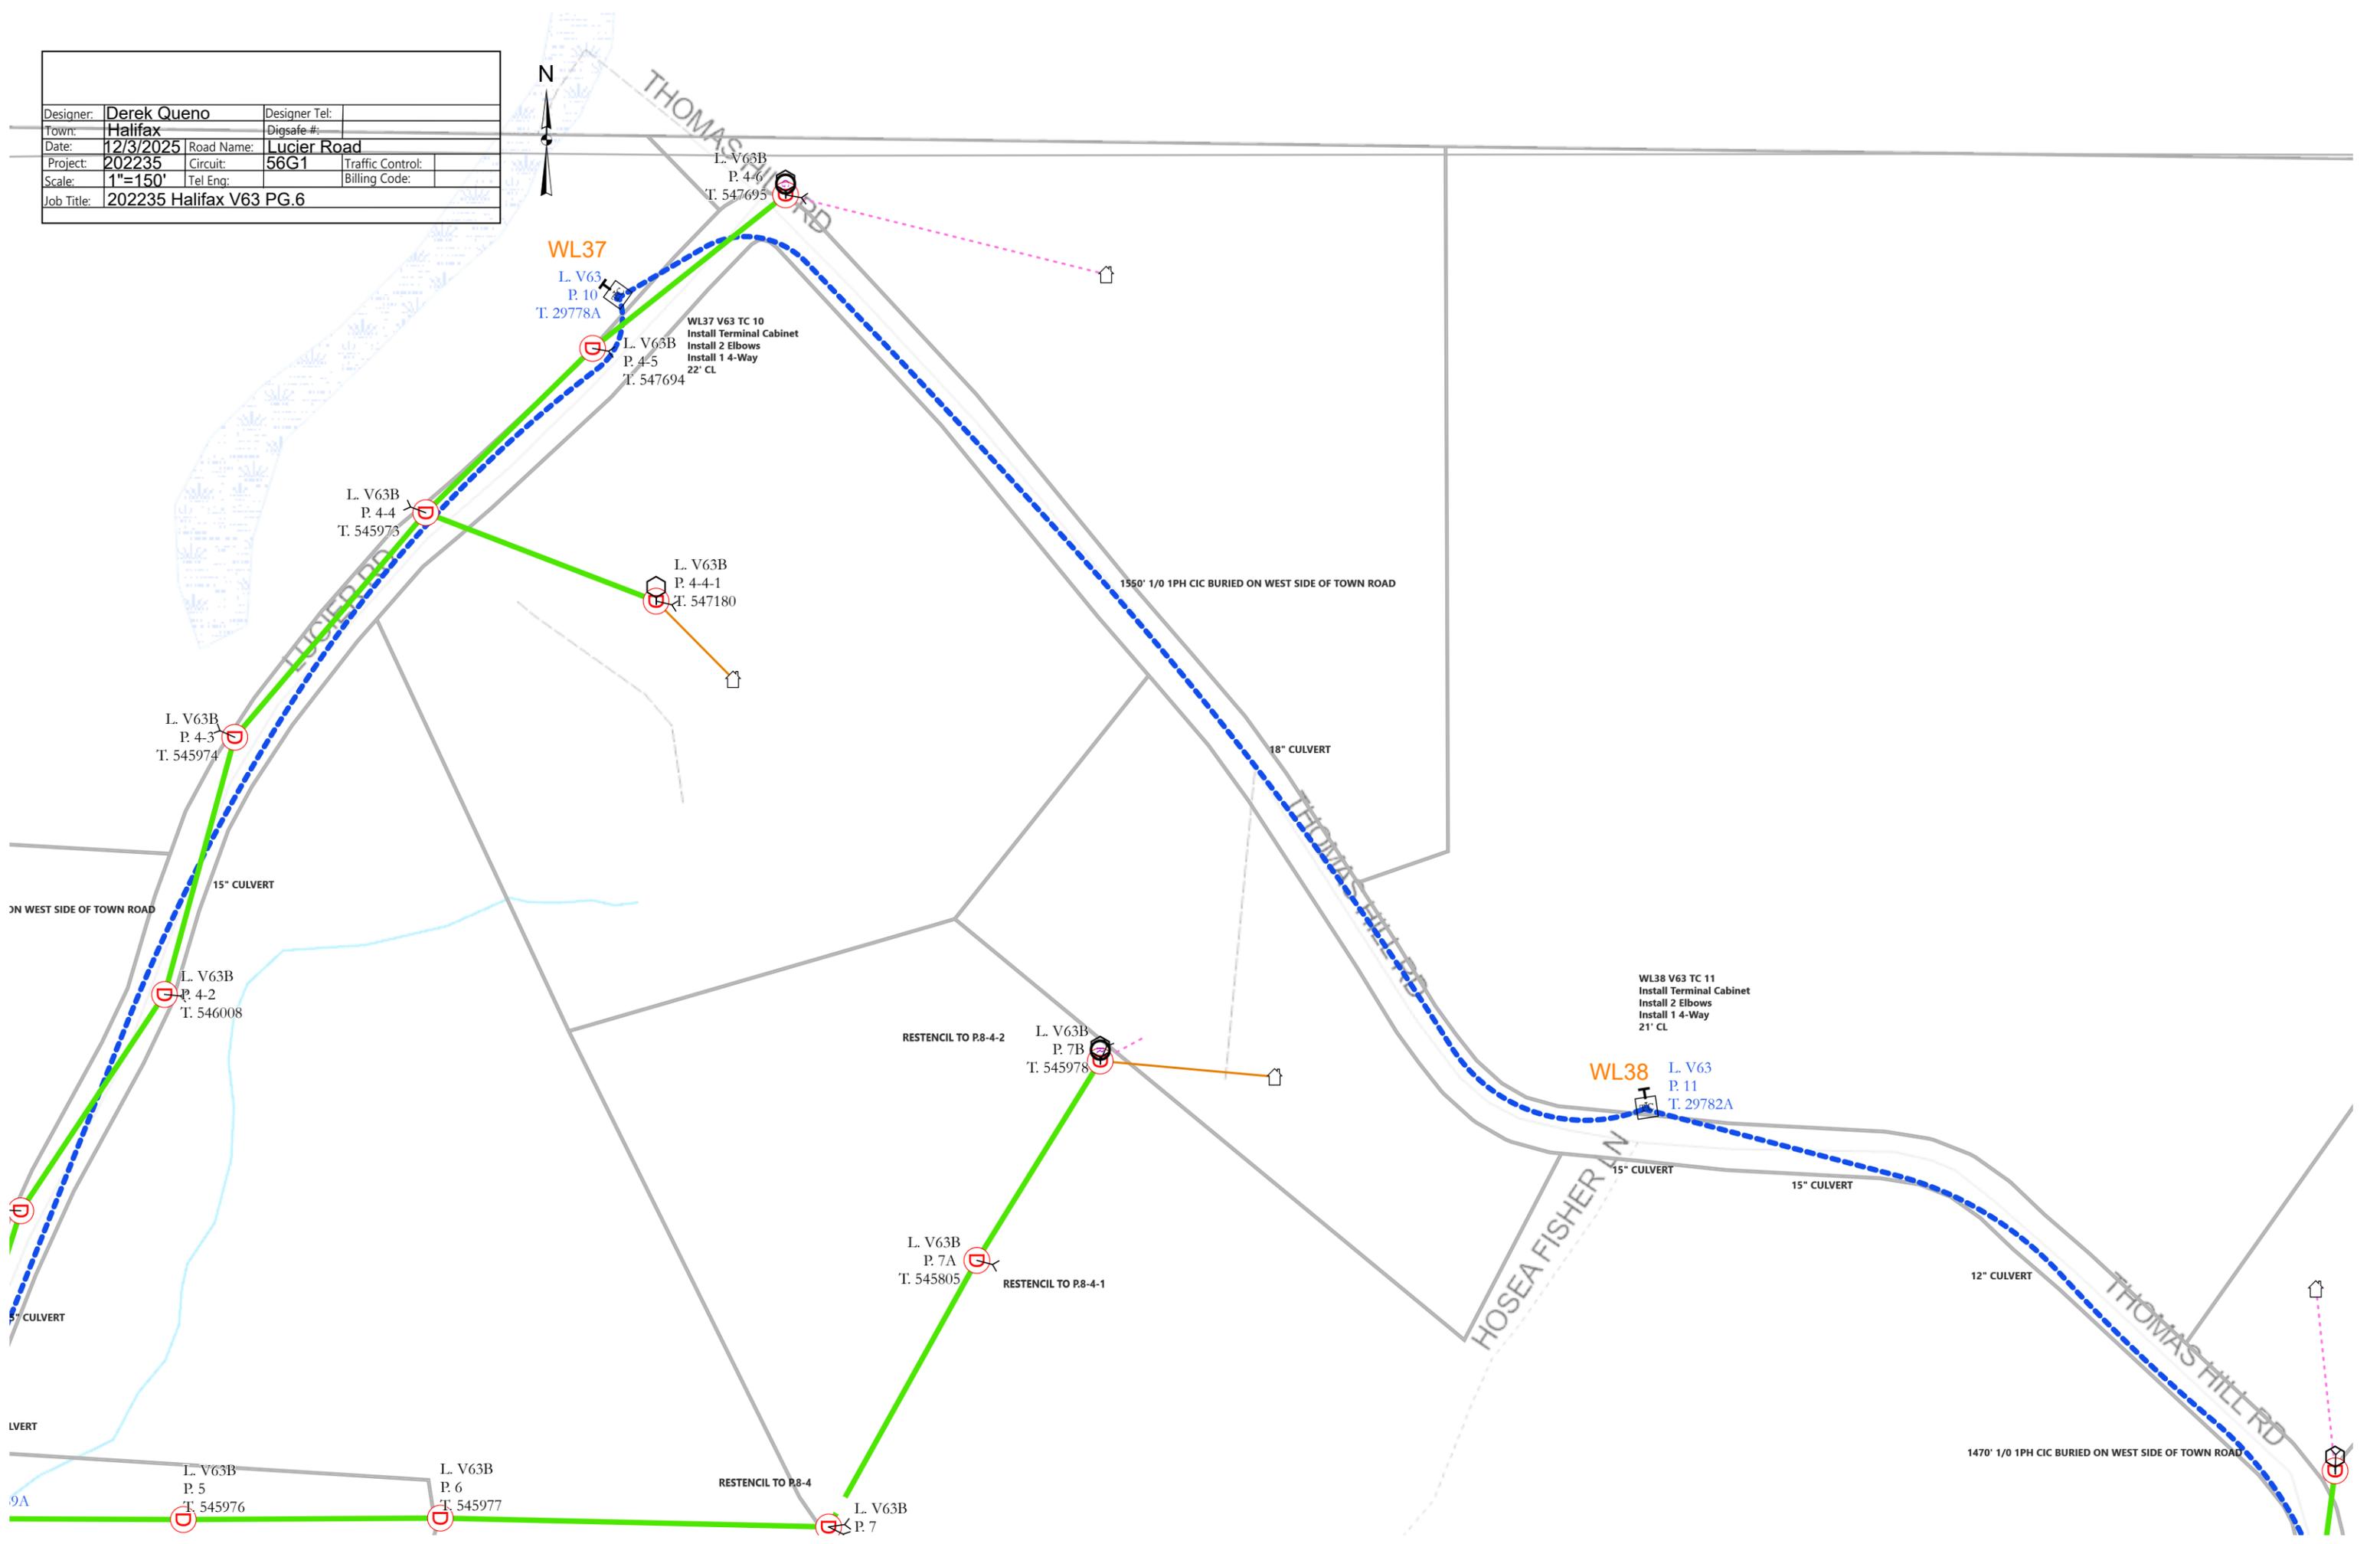

WL37

L. V63B
P. 10
T. 29778A

WL37 V63 TC 10
Install Terminal Cabinet
Install 2 Elbows
Install 1 4-Way
22' CL

L. V63B
P. 4-5
T. 547694

L. V63B
P. 4-4
T. 545973

L. V63B
P. 4-4-1
T. 547180

L. V63B
P. 4-3
T. 545974

L. V63B
P. 4-2
T. 546008

RESTENCIL TO P8-4-2

L. V63B
P. 7B
T. 545978

WL38

L. V63
P. 11
T. 29782A

WL38 V63 TC 11
Install Terminal Cabinet
Install 2 Elbows
Install 1 4-Way
21' CL

L. V63B
P. 7A
T. 545805

RESTENCIL TO P8-4-1

12" CULVERT

THOMAS HILL RD

1470' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

L. V63B
P. 5
T. 545976

L. V63B
P. 6
T. 545977

RESTENCIL TO P8-4

L. V63B
P. 7
T. 545977

1550' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

18" CULVERT

15" CULVERT

15" CULVERT

HOSEA FISHER LN


ON WEST SIDE OF TOWN ROAD

15" CULVERT

LVERT

9A

Designer:	Derek Queno	Design: Pencil to P.8-4-1		
Town:	Halifax	Digsafe #:		
Date:	12/3/2025	Road Name:	Lucier Road	
Project:	202235	Circuit:	56G1	Traffic Control:
Scale:	1"=150'	Tel. Eng.:		Billing Code:
Job Title:	202235 Halifax V63 PG.6			

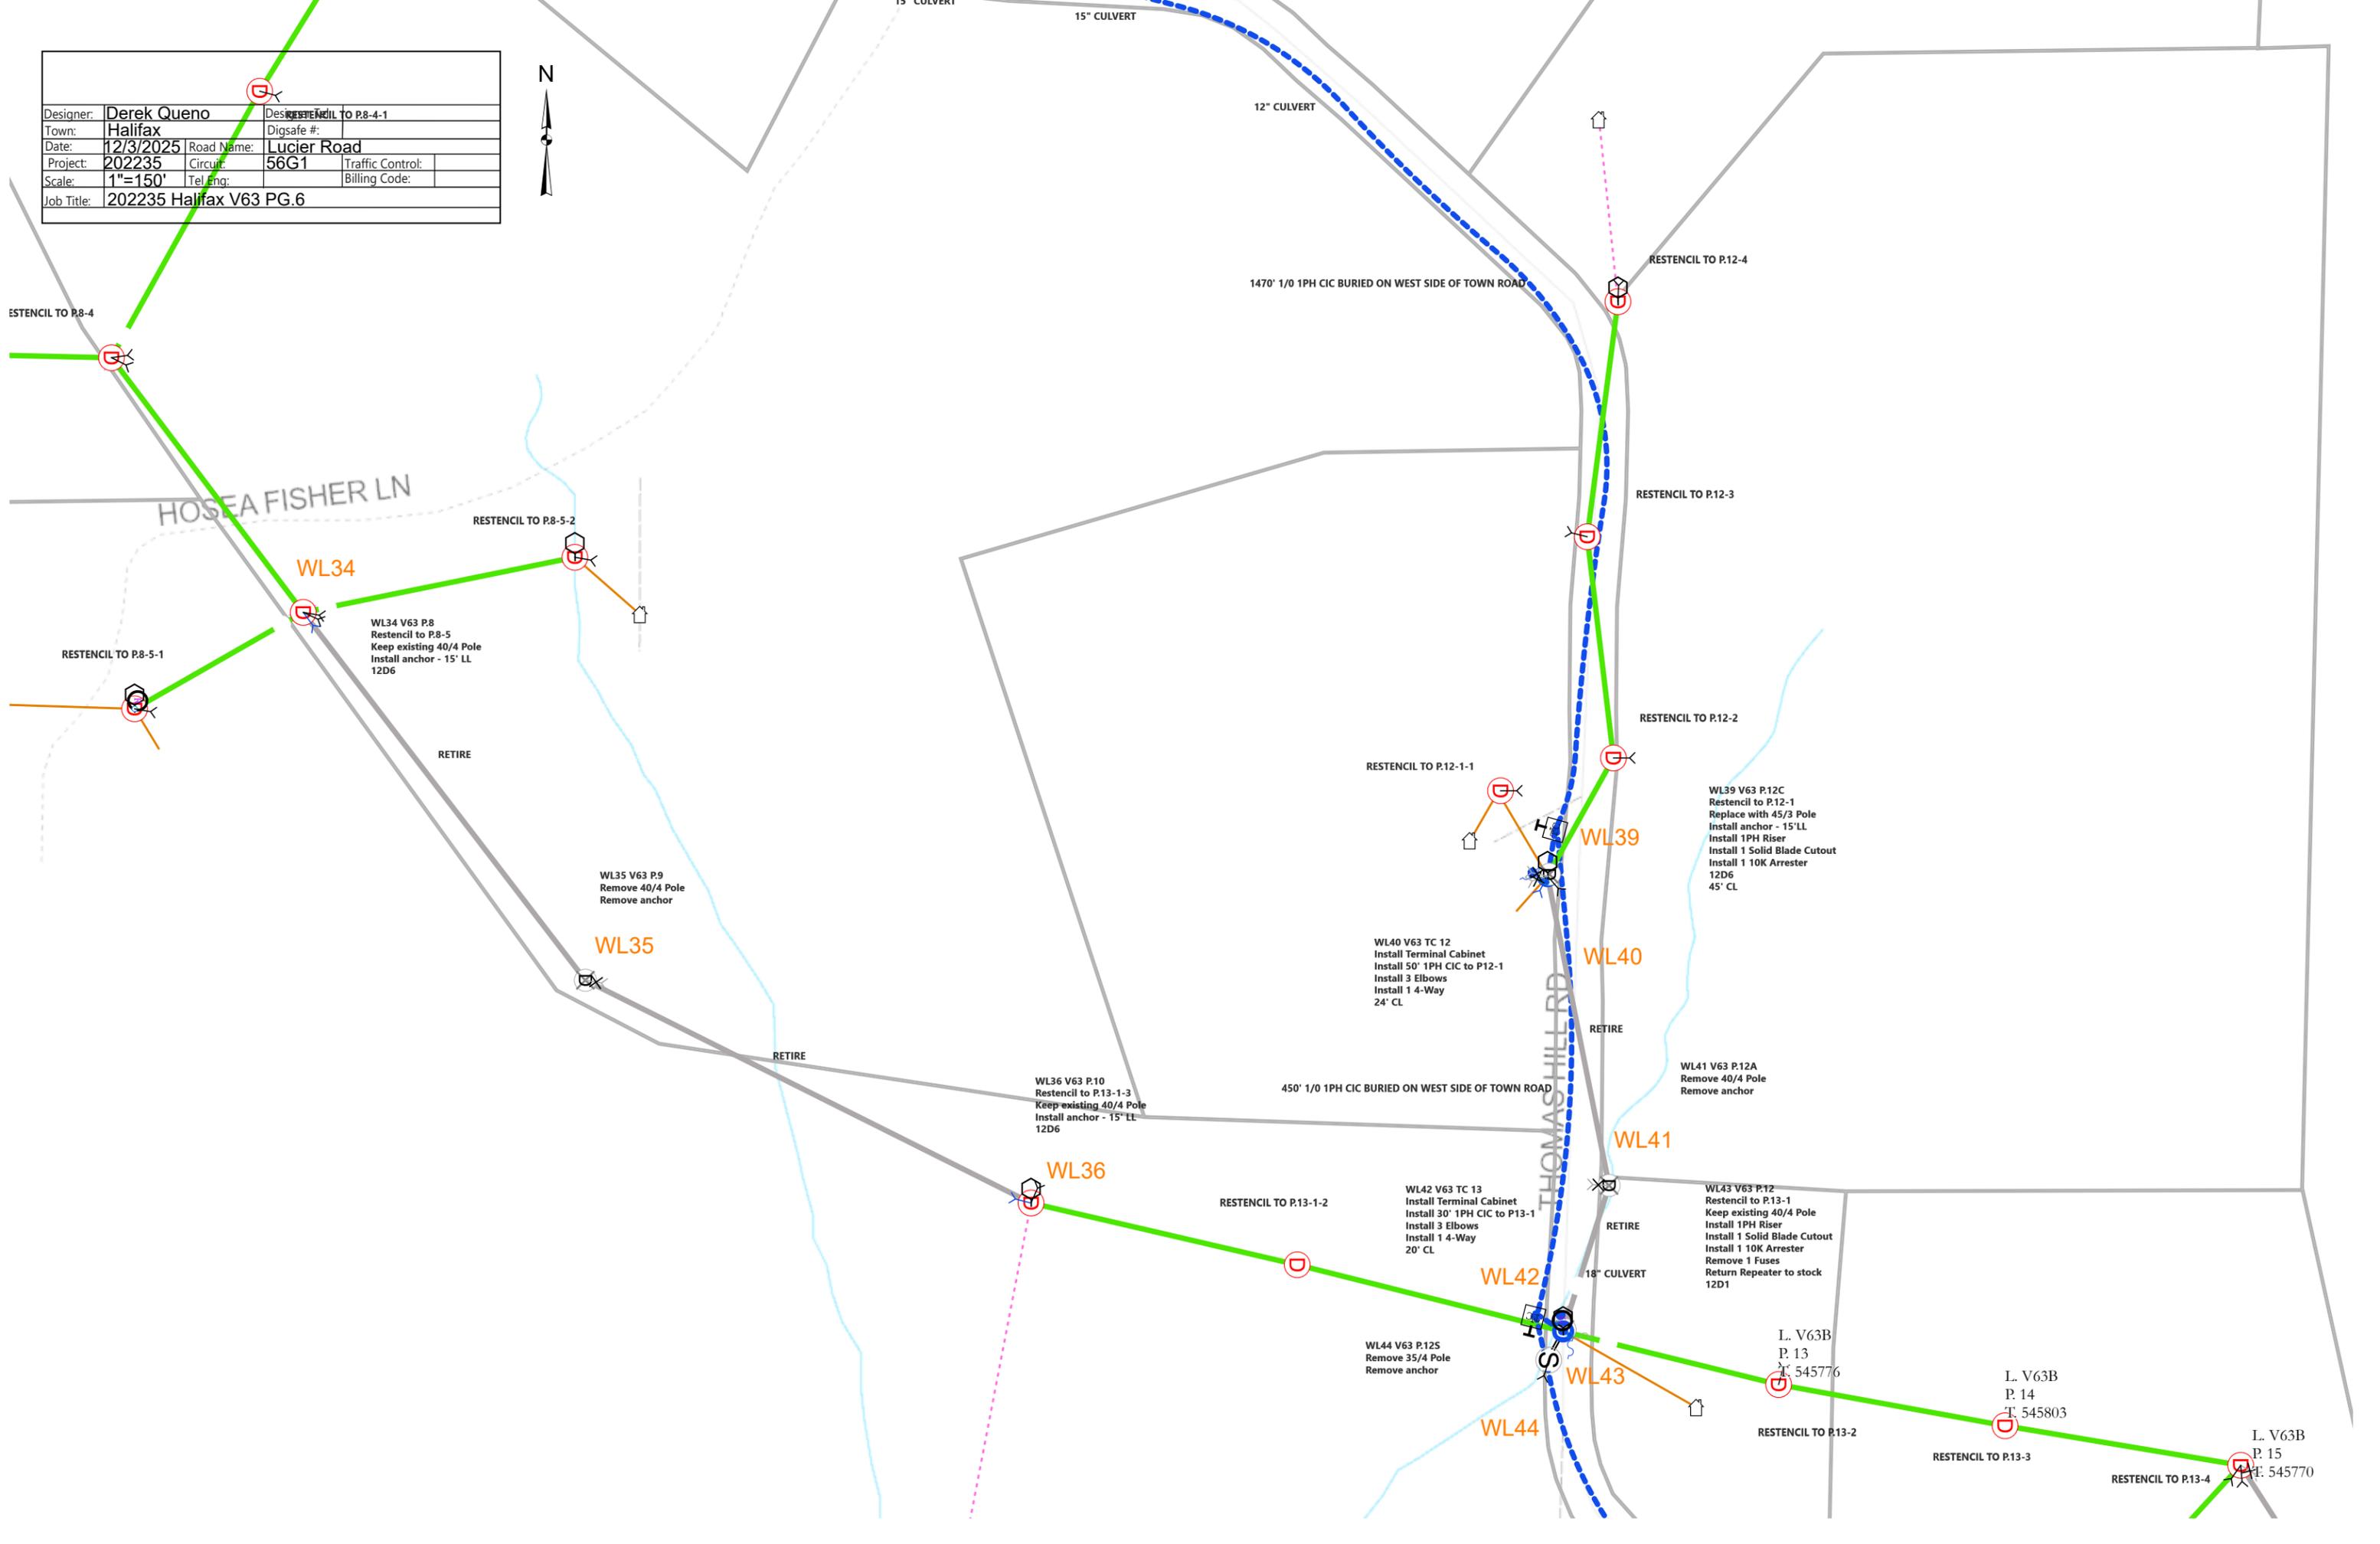

ESTENCIL TO P.8-4

HOSEA FISHER LN

WL34

WL34 V63 P.8
Restencil to P.8-5
Keep existing 40/4 Pole
Install anchor - 15' LL
12D6

RESTENCIL TO P.8-5-1

RETIRE

WL35 V63 P.9
Remove 40/4 Pole
Remove anchor

WL35

RETIRE

WL36 V63 P.10
Restencil to P.13-1-3
Keep existing 40/4 Pole
Install anchor - 15' LL
12D6

WL36

RESTENCIL TO P.13-1-2

WL40 V63 TC 12
Install Terminal Cabinet
Install 50' 1PH CIC to P.12-1
Install 3 Elbows
Install 1 4-Way
24' CL

WL40

RETIRE

450' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

WL41

WL41 V63 P.12A
Remove 40/4 Pole
Remove anchor

WL42 V63 TC 13
Install Terminal Cabinet
Install 30' 1PH CIC to P.13-1
Install 3 Elbows
Install 1 4-Way
20' CL

WL42

RETIRE

18" CULVERT

WL43 V63 P.12
Restencil to P.13-1
Keep existing 40/4 Pole
Install 1PH Riser
Install 1 Solid Blade Cutout
Install 1 10K Arrester
Remove 1 Fuses
Return Repeater to stock
12D1

WL43

WL44 V63 P.12S
Remove 35/4 Pole
Remove anchor

WL44

L. V63B
P. 13
T. 545776

RESTENCIL TO P.13-2

L. V63B
P. 14
T. 545803

RESTENCIL TO P.13-3

L. V63B
P. 15
T. 545770

RESTENCIL TO P.13-4

12" CULVERT

15" CULVERT

15" CULVERT

1470' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

RESTENCIL TO P.12-4

RESTENCIL TO P.12-3

RESTENCIL TO P.12-2

RESTENCIL TO P.12-1-1

WL39

WL39 V63 P.12C
Restencil to P.12-1
Replace with 45/3 Pole
Install anchor - 15' LL
Install 1PH Riser
Install 1 Solid Blade Cutout
Install 1 10K Arrester
12D6
45' CL

THOMAS HILL RD

RETIRE

18" CULVERT

L. V63B
P. 13
T. 545776

L. V63B
P. 14
T. 545803

L. V63B
P. 15
T. 545770

Riser
Solid Blade Cutout
K Arrester

Designer:	Derek Queno	Designer Tel:	
Town:	Halifax	Digsafe #:	
Date:	12/3/2025	Road Name:	Lucier Road
Project:	202235	Circuit:	56G1
Scale:	1"=150'	Tel Eng:	
Job Title:	202235 Halifax V63 PG.7	Billing Code:	



P.13-1
40/4 Pole
Riser
Solid Blade Cutout
K Arrester
uses
later to stock

L. V63B
P. 13
T. 545776

RESTENCIL TO P.13-2

L. V63B
P. 14
T. 545803

RESTENCIL TO P.13-3

L. V63B
P. 15
T. 545770

RESTENCIL TO P.13-4

RETIRE

WL45 V63 P.16
Remove 35/4 Pole

WL45

L. V63B
P. 16
T. 545806

RETIRE

THOMAS RIVER

15" CULVERT

WL47

L. V63B
P. 18
T. 493656

L. V63
P. 14
T. 29802A
WL48

WL48 V63 P.18
Restencil to P.14-1
Keep existing 40/4 Pole
Install 1PH Riser
Install 1 Solid Blade Cutout
Install 1 10K Arrester
12D6



L. V63B
P. 19A
T. 493598

1460' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

18" CULVERT

RETIRE

WL50

L. V63B
P. 21
T. 546062

WL50 V63 P.21
Remove 35/7 Pole



WL52

18" CULVERT

RESTENCIL TO P.13-5

L. V63B
P. 15A
T. 545804



18" CULVERT

1600' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

L. V63B
P. 15AS
T. 545807



L. V63B
P. 17
T. 547177

WL46

WL46 V63 P.17
Remove 40/4 Pole
Remove 2 Anchors

RETIRE

WL47 V63 TC 14
Install Terminal Cabinet
Install 25' 1PH CIC to P.14-1
Tap UG PRI from P.18 to TC
Install 3 Elbows
Install 1 4-Way
24' CL

WL49

L. V63B
P. 20
T. 493655




WL49 V63 P.20
Restencil to P.14-3
Keep existing 40/4 Pole
Install anchor - 15' LL
12D6



L. V63B
P. 20
T. 493655

Designer:	Derek Queno	Designer Tel:	
Town:	Halifax	Digsafe #:	
Date:	12/10/2025	Road Name:	Lucier Road
Project:	202235	Circuit:	56G1
Scale:	1"=150'	Tel Eng:	
Job Title:	202235 Halifax V63 PG.9		

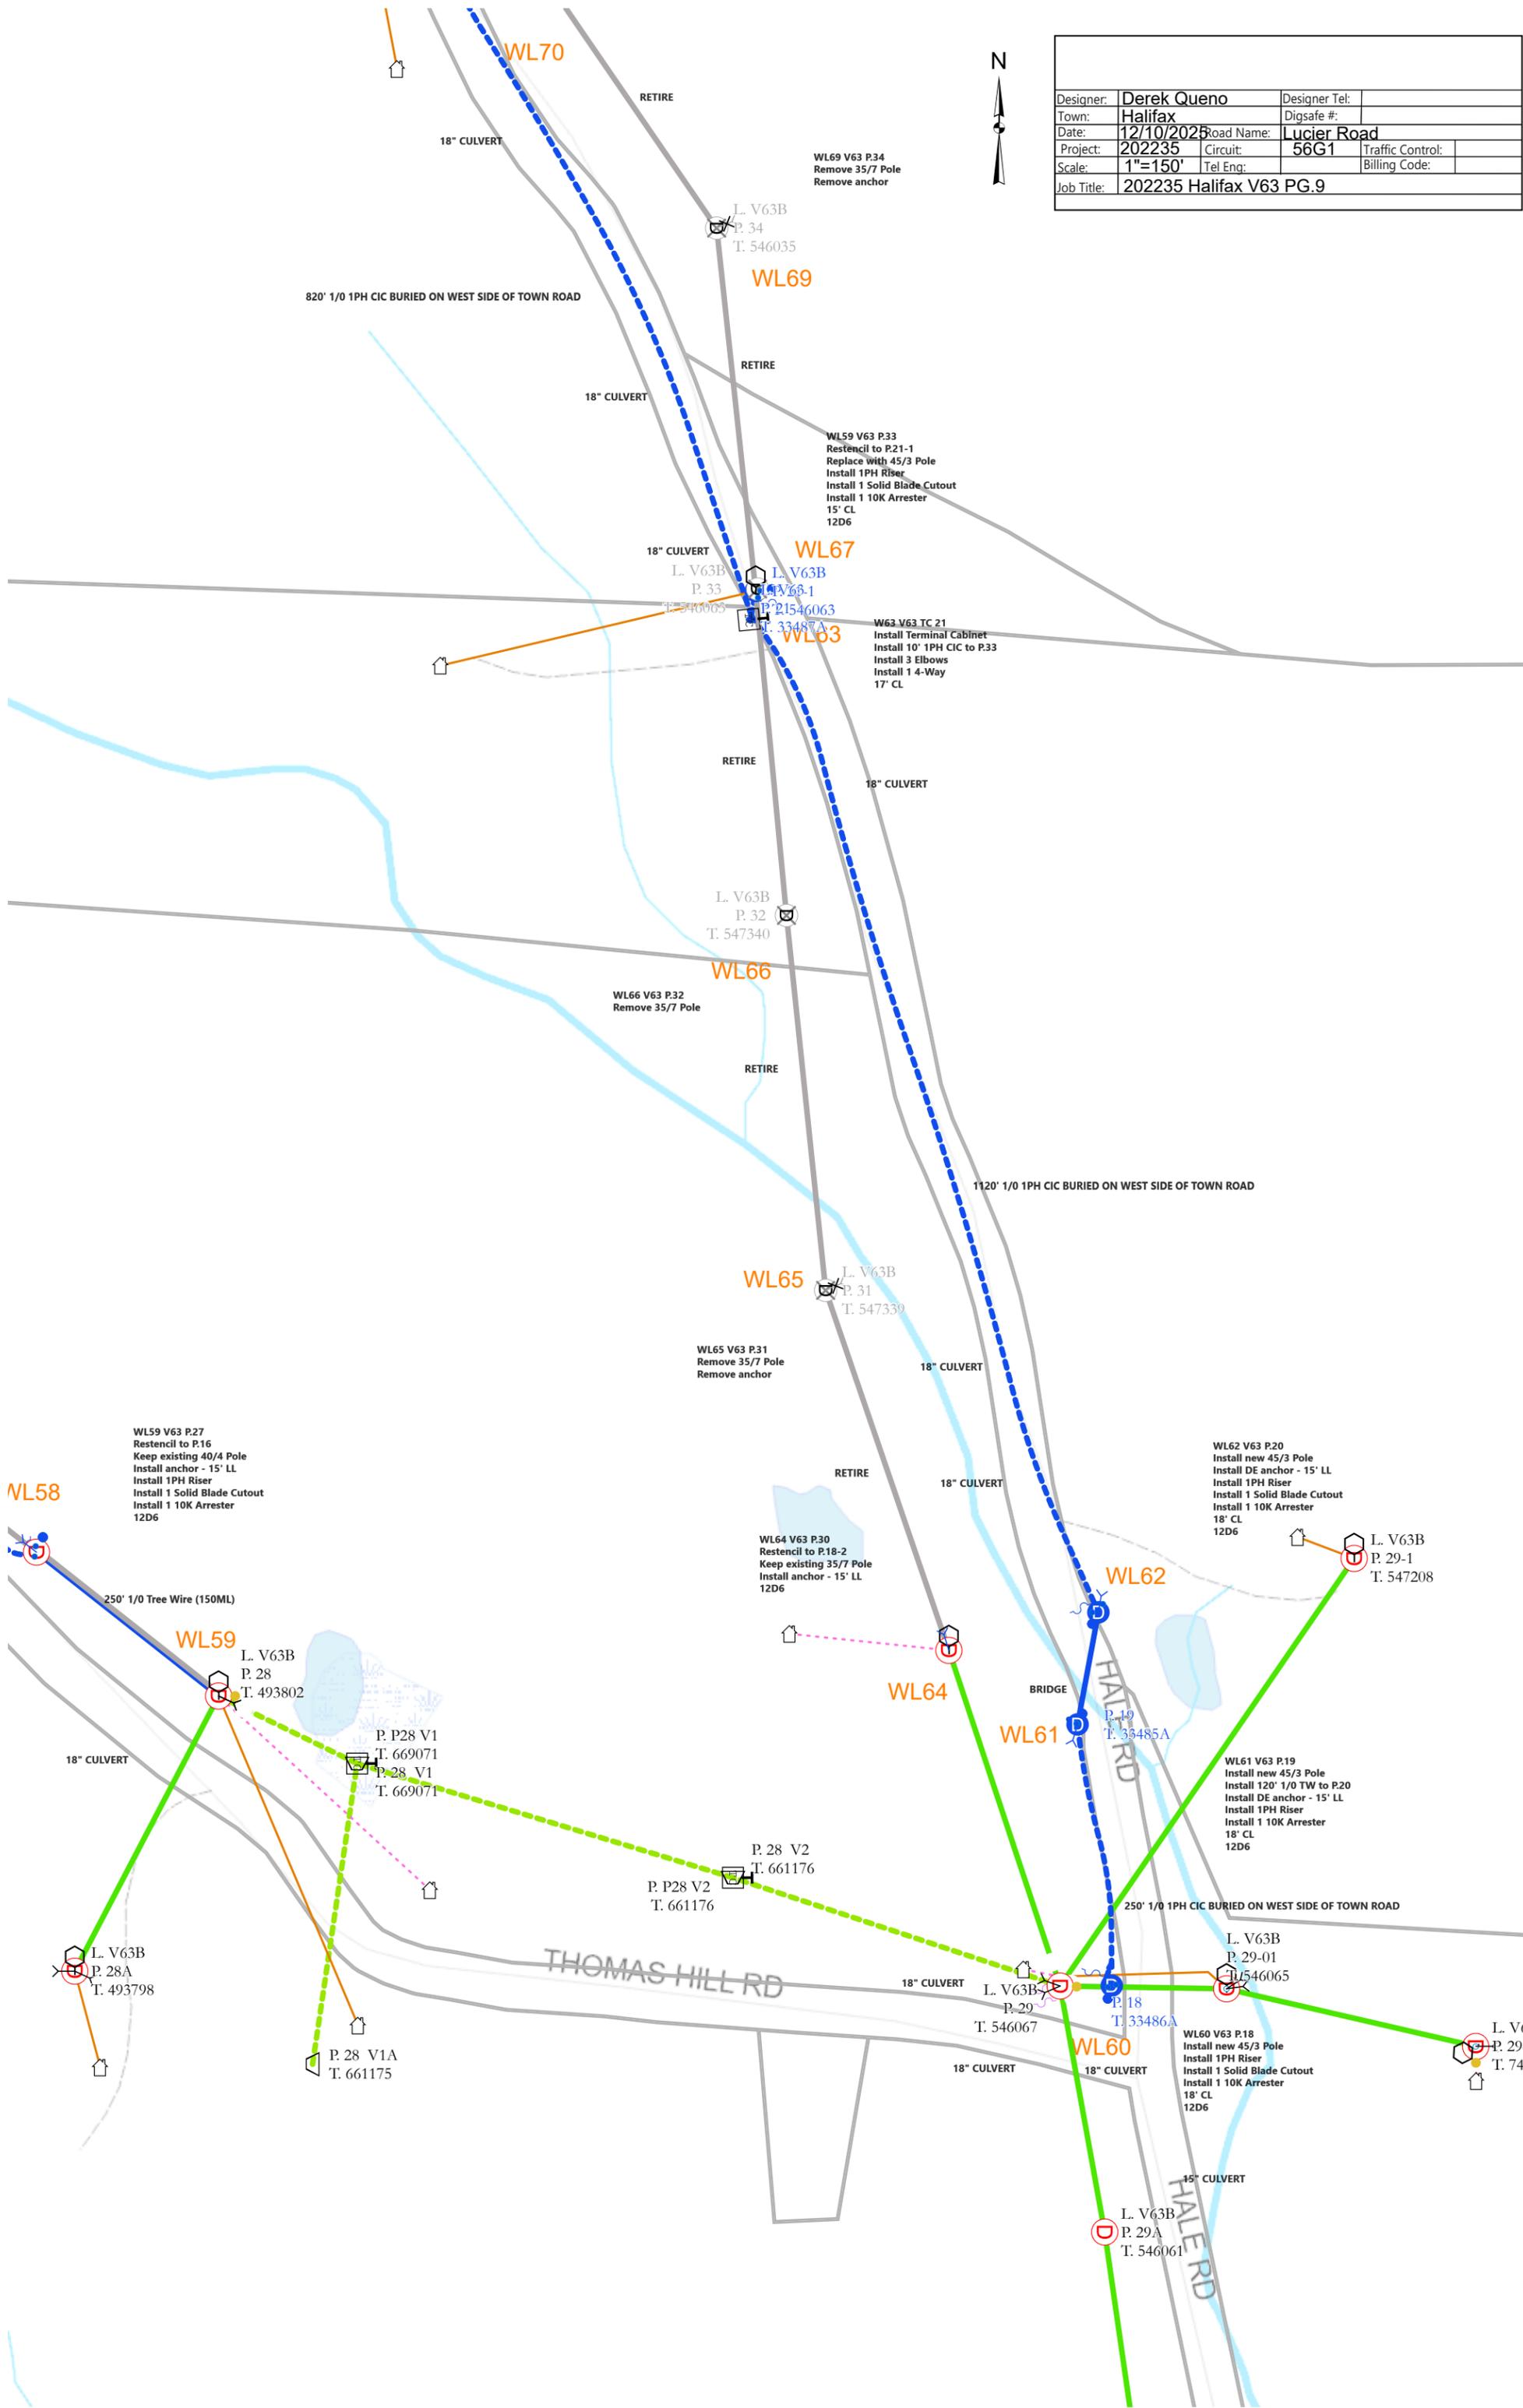

WL58
 WL59 V63 P.27
 Restencil to P.16
 Keep existing 40/4 Pole
 Install anchor - 15' LL
 Install 1PH Riser
 Install 1 Solid Blade Cutout
 Install 1 10K Arrester
 12D6

WL59
 L. V63B
 P. 28
 T. 493802

P. P28 V1
 T. 669071
 P. P28 V1
 T. 669071

L. V63B
 P. 28A
 T. 493798

P. 28 V1A
 T. 661175

P. P28 V2
 T. 661176
 P. P28 V2
 T. 661176

THOMAS HILL RD

WL65
 WL65 V63 P.31
 Remove 35/7 Pole
 Remove anchor

WL64
 WL64 V63 P.30
 Restencil to P.18-2
 Keep existing 35/7 Pole
 Install anchor - 15' LL
 12D6

WL66
 WL66 V63 P.32
 Remove 35/7 Pole

WL67
 WL67 V63 P.33
 Restencil to P.21-1
 Replace with 45/3 Pole
 Install 1PH Riser
 Install 1 Solid Blade Cutout
 Install 1 10K Arrester
 15' CL
 12D6

WL69
 WL69 V63 P.34
 Remove 35/7 Pole
 Remove anchor

WL63
 WL63 V63 TC 21
 Install Terminal Cabinet
 Install 10' 1PH CIC to P.33
 Install 3 Elbows
 Install 1 4-Way
 17' CL

WL65
 L. V63B
 P. 31
 T. 547339

WL64

WL61
 L. V63B
 P. 19
 T. 33485A

WL62
 WL62 V63 P.20
 Install new 45/3 Pole
 Install DE anchor - 15' LL
 Install 1PH Riser
 Install 1 Solid Blade Cutout
 Install 1 10K Arrester
 18' CL
 12D6

L. V63B
 P. 29-1
 T. 547208

WL61
 WL61 V63 P.19
 Install new 45/3 Pole
 Install 120' 1/0 TW to P.20
 Install DE anchor - 15' LL
 Install 1PH Riser
 Install 1 10K Arrester
 18' CL
 12D6

L. V63B
 P. 29-01
 T. 546065

WL60
 WL60 V63 P.18
 Install new 45/3 Pole
 Install 1PH Riser
 Install 1 Solid Blade Cutout
 Install 1 10K Arrester
 18' CL
 12D6

L. V63B
 P. 29A
 T. 546061

L. V63B
 P. 29-
 T. 74

HALE RD

HALE RD

BRIDGE

820' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

1120' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

250' 1/0 Tree Wire (150ML)

250' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

RETIRE

RETIRE

RETIRE


RETIRE

RETIRE

18" CULVERT

15" CULVERT

Designer:	Derek Queno	Designer Tel:	
Town:	Halifax	Digsafe #:	
Date:	12/10/2025	Road Name:	Lucier Road
Project:	202235	Circuit:	56G1
Scale:	1"=150'	Tel Eng:	
Job Title:	202235 Halifax V63 PG.10		

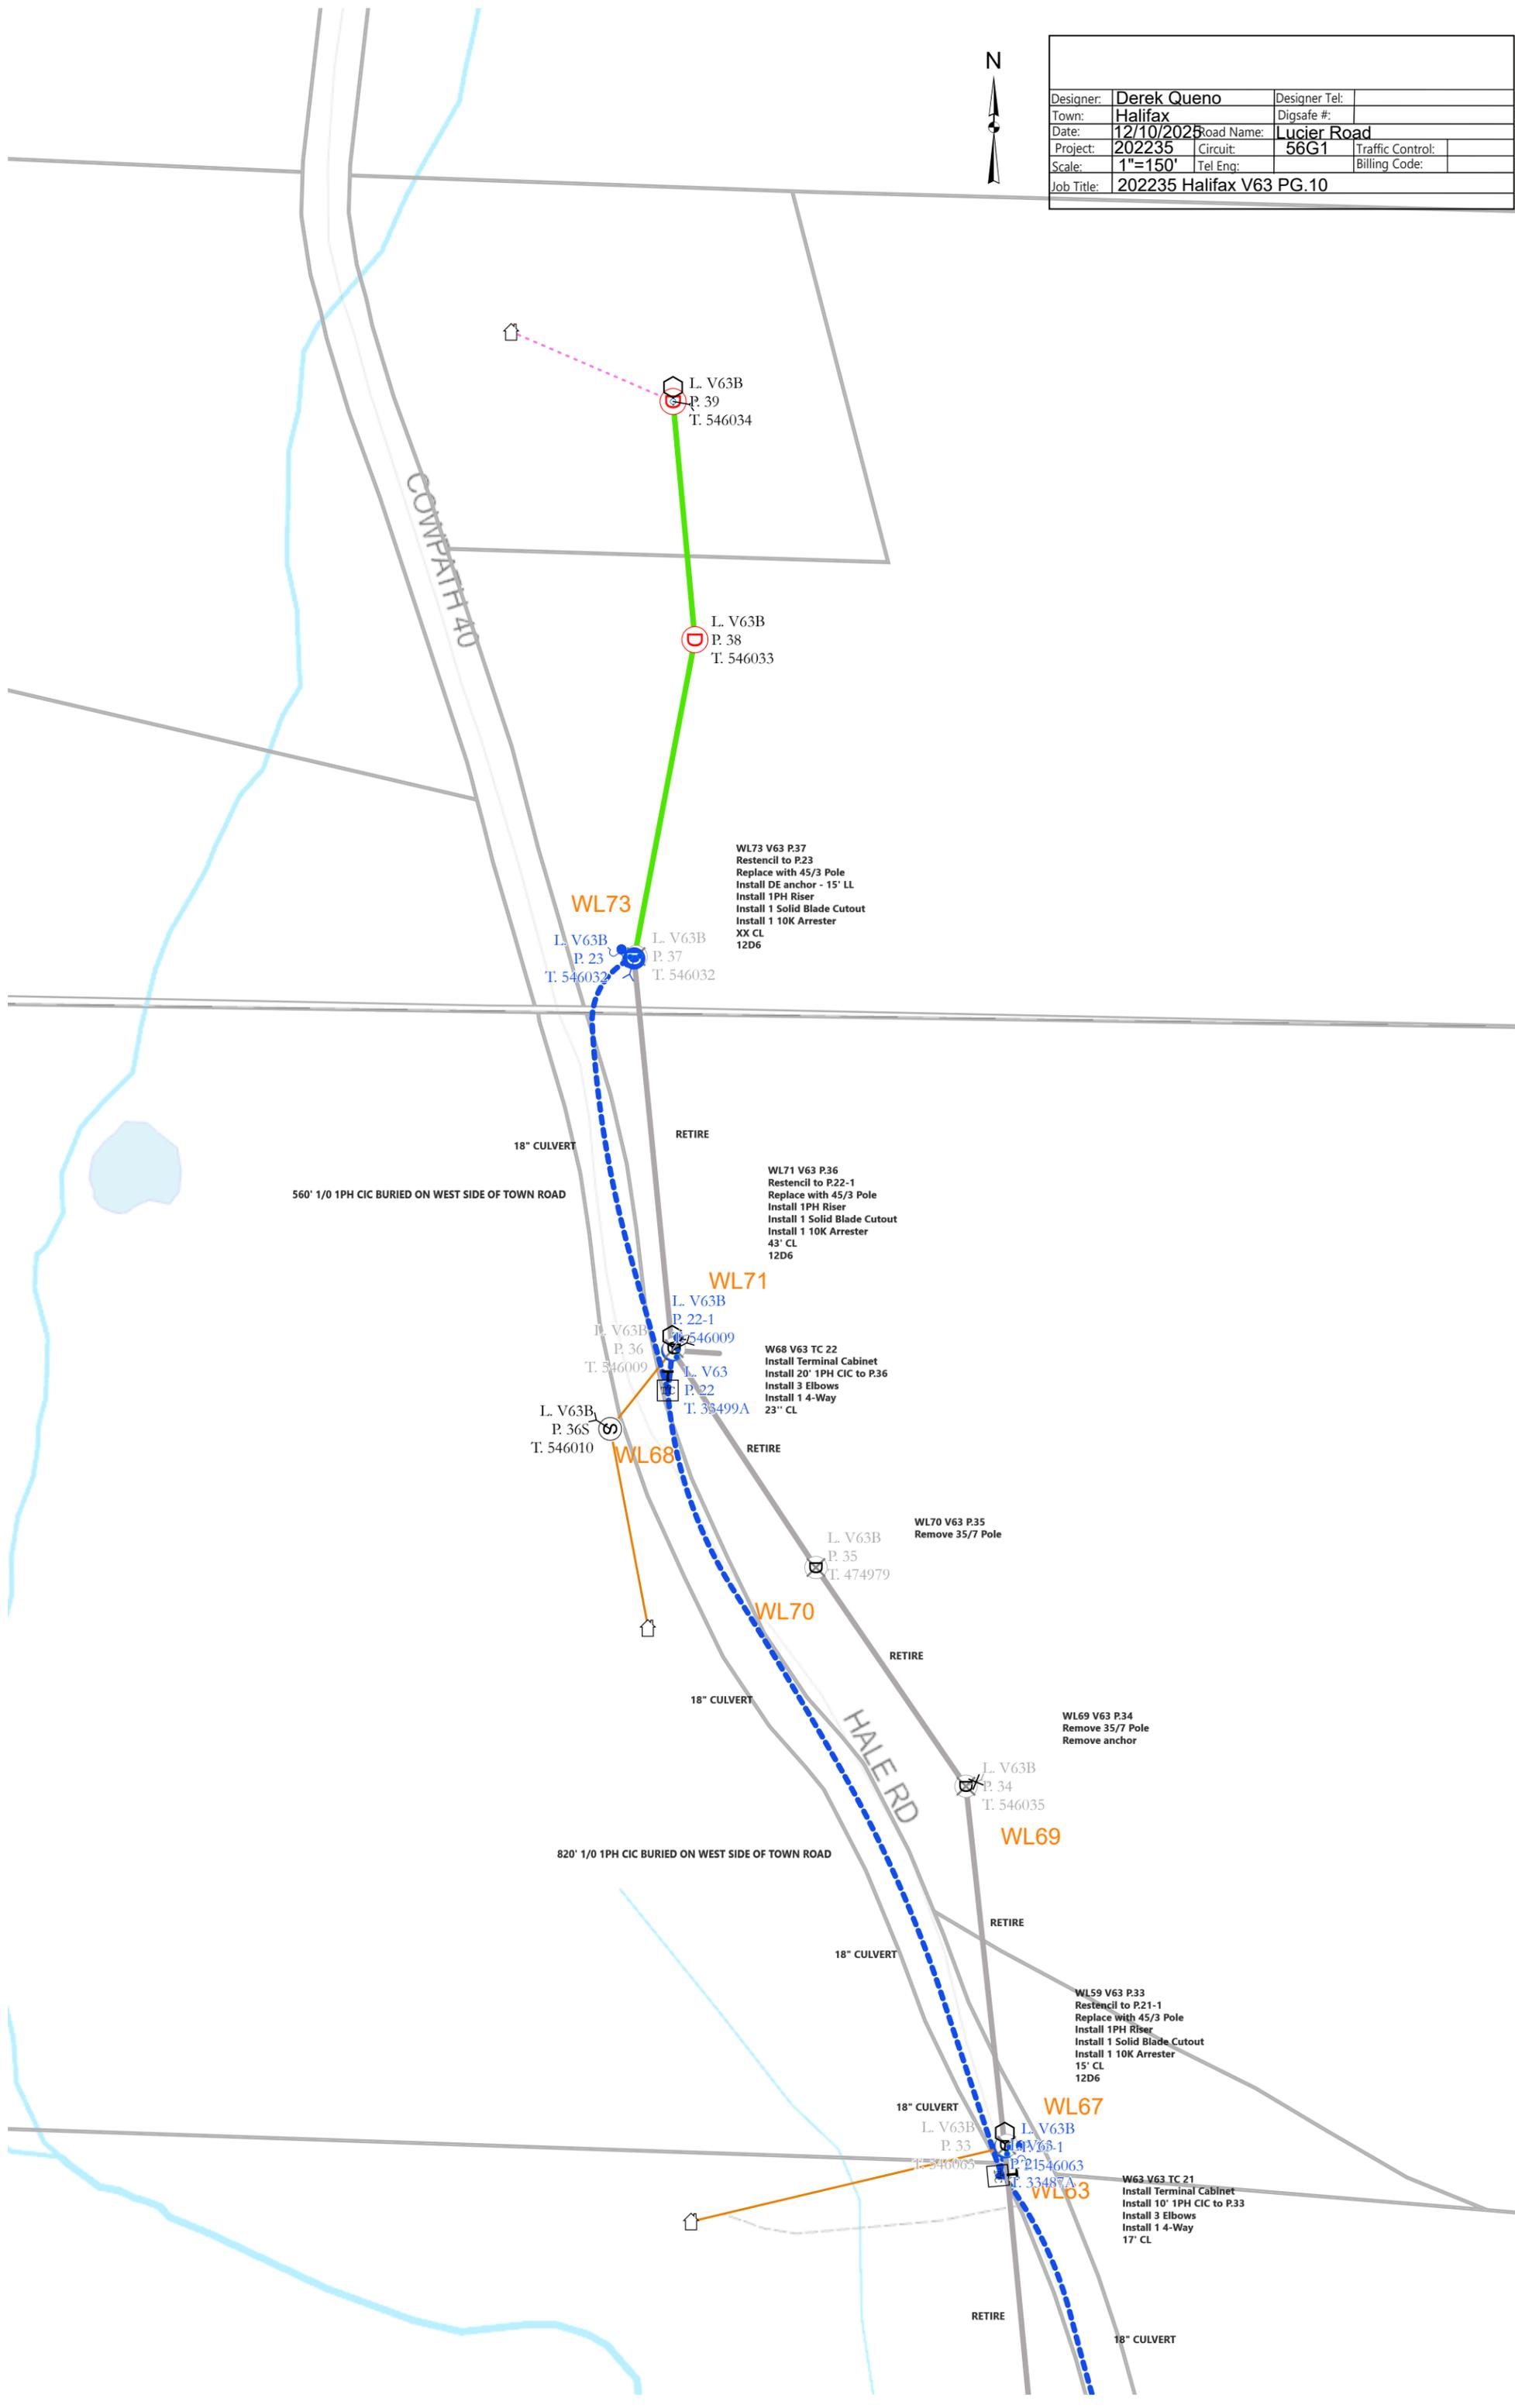

WL73 V63 P.37
 Restencil to P.23
 Replace with 45/3 Pole
 Install DE anchor - 15' LL
 Install 1PH Riser
 Install 1 Solid Blade Cutout
 Install 1 10K Arrester
 XX CL
 12D6

WL71 V63 P.36
 Restencil to P.22-1
 Replace with 45/3 Pole
 Install 1PH Riser
 Install 1 Solid Blade Cutout
 Install 1 10K Arrester
 43" CL
 12D6

W68 V63 TC 22
 Install Terminal Cabinet
 Install 20' 1PH CIC to P.36
 Install 3 Elbows
 Install 1 4-Way
 23" CL

WL69 V63 P.34
 Remove 35/7 Pole
 Remove anchor

WL59 V63 P.33
 Restencil to P.21-1
 Replace with 45/3 Pole
 Install 1PH Riser
 Install 1 Solid Blade Cutout
 Install 1 10K Arrester
 15' CL
 12D6

W63 V63 TC 21
 Install Terminal Cabinet
 Install 10' 1PH CIC to P.33
 Install 3 Elbows
 Install 1 4-Way
 17' CL

560' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

820' 1/0 1PH CIC BURIED ON WEST SIDE OF TOWN ROAD

18" CULVERT

RETIRE

18" CULVERT

RETIRE

18" CULVERT

RETIRE

18" CULVERT

RETIRE

18" CULVERT

COMPATH 40

HALE RD
